

# Review of County Development Plan 2004–2010

&

# Preparation of new Development Plan 2010-2016

Briefing for the County Council Meeting
October 2008



## Purpose



- Background
- Overview of process
- Strategic Environmental Assessment (SEA)
- Timeframe
- Consultation







- The Development Plan the policy context for planning at local level...
- Post 2000...spatial plans at city/county/local level have to complement plans at national & regional levels ...
- Challenges ...Europe...economic & population trends...competitiveness...quality of life...... accessibility...environmental pressures...climate change...energy efficiency...older built up areas...rural areas...




#### Overview 2 - 2000 Act



- Time Frame
  - every 6 years
  - 99 week review process
  - Stages pre-Draft, preparation of Draft Plan, material alterations, making of Plan
- Requirements within stages:
  - Public consultation
  - Manager's Report
  - Preparation of Plans (Proposed Draft, Draft, Amended Draft and Final Plan)
- Set out overall/core strategy for county
- ...for proper planning and sustainable development...
- Pre-Draft Consultation
- SEA parallel process within the 2 years
- Role of DOEHLG



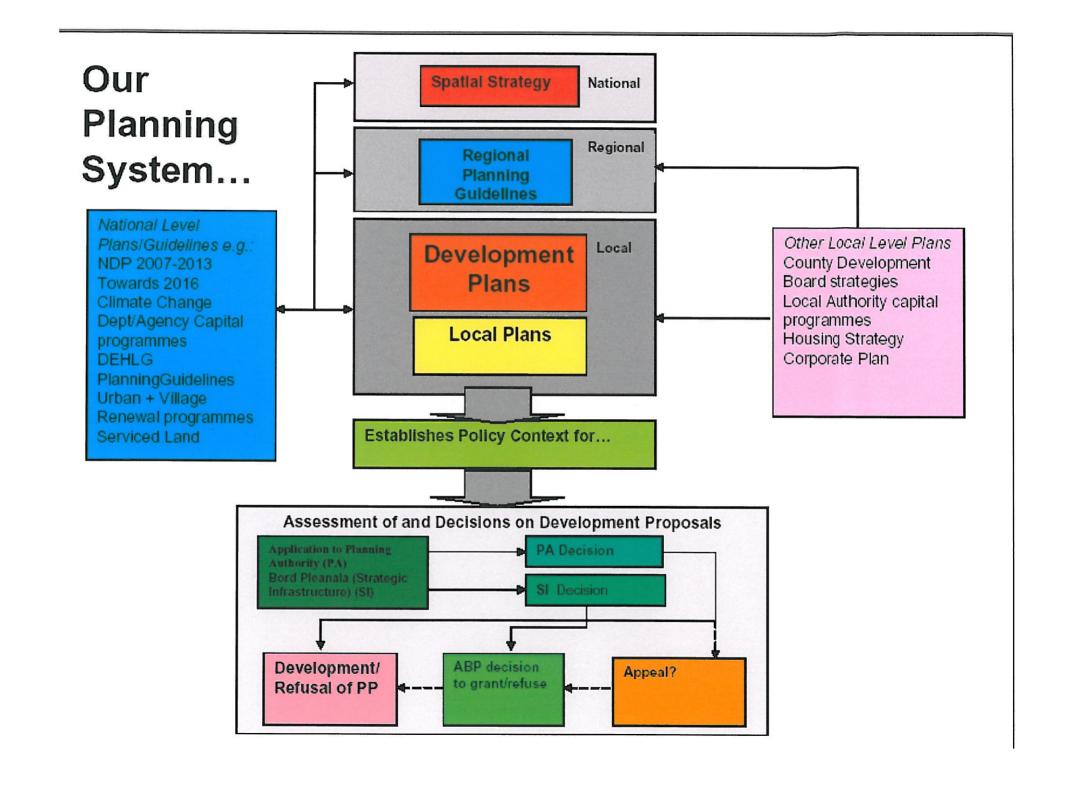





#### Dev. Plans should:

- Strategic core strategy, "big picture" strategic issues
- Set out framework within which <u>sustainable</u> development can be achieved
- Catalyst for positive change and progress
- Anticipate future needs on an <u>objective</u> basis
- Consistent with hierarchy of plans/strategies at different levels
- Protect / enhance environment / heritage
- Contain <u>background</u> detail
- · Be user friendly, logical, internally consistent & up to date
- Address <u>diverse</u> communities
- Observe codes of <u>conduct</u>
- Ownership central to implementation



## Inputs to New Plan



- Existing 2004-2010 Plan
- Mandatory Objectives 2000 Act e.g.
  - Zoning of land
  - Provision of infrastructure
  - Conservation and protection of the environment
  - Integration of planning & sustainable development with social, community & cultural requirements of area & its population
- National/Regional/Local plans/strategies/guidelines
- Public consultation process
- Service providers & prescribed bodies
- Members' Motions/Directions
- Planning & other Council Departments
- Background studies
- State of the Environment Report for SEA process



# National, regional & local - plans, policies & guidelines





#### For instance -

- National Development Plan
- National Spatial Strategy
- National Climate Change Strategy 2007-2012
- Regional Planning Guidelines (under review)
- CDB Strategy
- SDCC Plans LAPs, Adamstown SDZ, Tallaght LAP, Clonburris SDZ etc.
- DOEHLG Guidelines e.g.
  - · Strategic Environmental Assessment (SEA) Nov. 2004
  - · Development Plans June 2007
  - Quality Housing for Sustainable Communities 2007
  - · Design Standards for Apartments Sept. 2007
  - Sustainable Residential Development (Draft) Feb. 2008
  - Appropriate assessment implementation of Birds & Habitats Directives Feb. 2008
  - Provision of Schools July 2008
  - Flooding forthcoming
  - · National and strategic routes forthcoming



## **SEA** (1)







- P&D Act 2000 requires Plan to contain information on likely significant effects on the environment of implementing the plan
- SEA required for Development Plans 21<sup>st</sup> July 2004
- Environmental assessment
  - "the preparation of an environmental report,
  - the carrying out of consultations,
  - the taking into account of the environmental report and the results of the consultations in decision making and
  - the provision of information on the decision"



# SEA (2)







- Environmental Report
  - "identify, describe and evaluate the <u>likely significant</u> <u>effects</u> on the environment of implementing the plan or amended plan, and reasonable <u>alternatives</u>, taking account of the objectives and geographical scope of the plan"
- Environmental considerations need to be integrated from beginning rather than an assessment at end of process "If the SEA process is to add value to plan making, the preparation of the (Environmental) report must influence the choice of the preferred plan strategy, and of any mitigation measures..." (Guidelines p. 23)



# SEA & Plan Making Process







Stage	Plan	SEA
Pre-review	Prepare Working Papers	Preparatory work incl. baselines
Initial Public Consultation	(a) Statutory notice (b) Issues Paper	Scope Environmental Report
Preparation of Documentation	Prepare Draft Plan	Prepare Environmental Report
Public Consultation	Display Draft Plan / consideration of submissions	Environmental Report / consideration of submissions
2nd Display (if required)	Display of any Material Amendment(s) to Draft Plan	Identify any significant environmental effects of such material amendment(s)
Completion of Process	Adoption of plan	Make specified information available
Post Plan	Implementation	Monitor



## Appropriate Assessment







- European Court Ireland didn't correctly transpose Article 6(3) and (4) of Habitats Directive by not
  providing explicitly for appropriate assessment of land use plans
- Development plans must be screened for any potential impact on areas designated as Natura 2000 sites – (Special Areas of Conservation (SACs) or Special Protection Areas (SPAs)).
- Two SACs in SDCC -
  - Glenasmol Valley and
  - Wicklow Mountains (part of)
- Where, following screening, it is found that the draft plan may have an impact on the conservation objectives of a Natura 2000 site or that such an impact cannot be ruled out, adopting a precautionary approach an appropriate assessment of the plan must be carried out.
- Impacts assessed must include indirect and cumulative impacts of approving the plan, considered with any current or proposed activities, developments or policies impacting on the site.
- The potential impacts of policies outside Natura 2000 sites but potentially impacting upon them ('ex situ' impacts) must also be included in the assessment.
- Guidelines to issue from DOEHLG



#### Review of Plan 2004-2010



- Adopted on 10th November 2004
- Effective on 8th December 2004
- Expires on 7th December 2010
- Review process must start within 4 years of making Plan i.e. by 7th November 2008
- Start date may be amended



ID	0	Task Name	Duration	Start	Finish	y 01 December   11 April   21 August   01 January   11 May   21 September   01/09   03/11   05/01   09/03   11/05   13/07   14/09   16/11   18/01   22/03   24/05   26/07   27/09   29/1
1		Public Notice of intention to prepare Plan	1 day	Fri 07/11/08	Fri 07/11/08	Staff
2	H	Pre-Draft Public Consultation (extended by 1 week)	9 wks	Fri 07/11/08	Thu 08/01/09	Public
3		Christmas 2008	1.6 wks	Wed 24/12/08	Fri 02/01/09	
4	11 1	Preparation of Manager's Report to Clirs on Pre-Draft Consultation	7 wks	Fri 09/01/09	Thu 26/02/09	Staff
5		Consideration of Manager's Report and Issue of Directions by	10 wks	Fri 27/02/09	Thu 07/05/09	Councillors
6		Preparation of Proposed Draft Plan by Staff	12 wks	Fri 08/05/09	Thu 30/07/09	Staff
7	п	Local elections (approx.)	1 day	Thu 11/06/09		
8	п	Consideration of Proposed Draft Plan by Cllrs	8 wks	Fri 31/07/09	Thu 24/09/09	Councillors
9		Send Notice of Draft Plan preparation and publish copy of	2 wks	Fri 25/09/09	Thu 08/10/09	Staff
10		Draft Plan Public Consultation	10 wks	Fri 09/10/09	Thu 17/12/09	Public
11	п	Christmas 2009	1.6 wks	Thu 24/12/09	Mon 04/01/10	
12	п	Prepare CM's Report to Clirs on Draft Plan Consultation	12 wks	Fri 18/12/09	Thu 11/03/10	Staff
13		Consideration of CM's report on Draft Plan Consultation	12 wks	Fri 12/03/10	Thu 03/06/10	Councillors
14	п	Making of Plan or Material Alterations to Draft Plan	1 day	Thu 03/06/10		Councillors
15		Giving notice of Plan or Material Alterations to Draft	3 wks	Fri 04/06/10	Thu 24/06/10	Staff
16		Public consultation on Material Alterations	4 wks	Fri 25/06/10	Thu 22/07/10	Public
17		CM's Report to Cllrs on Submissions received on	4 wks	Fri 23/07/10	Thu 19/08/10	Staff
18	п	Consideration of CM's Report on Alterations and making of Plan	6 wks	Fri 20/08/10	Thu 30/09/10	Councillors
19	11 1	Make Plan	1 day	Thu 30/09/10		<b>→</b> 30/09
20	п	Prepare Plan for Publication and publish	20 days	Fri 01/10/10	Thu 28/10/10	Staff
21	п	2010-2016 Plan becomes effective	1 day	Thu 28/10/10		
22	п	Latest date for 2004-2010 Plan to expire	1 day			
	125		ian to	ian to 1 day		

### **Timeframe**



Preparation of Plan - 4 stages

Stage 1	Pre-draft	26 weeks	Early Nov. 2008  – early May 2009
Stage 2	Preparation of Draft Plan	20 weeks	Early May 2009  – end Sept. 2009
Stage 3	Draft Plan	36 weeks	End Sept. 2009 – early June 2010
Stage 4	Material Changes & Adoption of Plan	17 weeks	Early June 2010  – end Sept. 2010

#### Requirements within each stage:

- •Public Consultation (except stage 2)
- •Manager's Report / Recommendations
- Member's Directions/Decisions



### Pre-Draft Consultation











- Aim of public consultation
  - Ascertain the views of the widest range of individuals, interest groups and organisations who have an interest in the proper planning and sustainable development of the county.
- Views on the 'big picture' or strategic issues facing the county will be sought at the pre-draft stage.
- Pre-Draft consultation stage from 4<sup>th</sup> Nov. 2008 to 8<sup>th</sup> Jan. 2009
- Consultation programme -
  - Adverts, in local and national papers inviting written submissions
  - Use of other media
  - Inform community groups of the process
  - Hold public consultation meetings local groups invited 5 evening meetings in Ballyroan, Rathcoole, Clondalkin, Lucan and Tallaght Venues and number of meetings mirror that of the County Heritage Plan Consultation
  - Letters to & contact with prescribed bodies and service providers
- Information dissemination to include -
  - Background Issues Paper/Brochure
  - Guide to Making a Submission
  - Information on www.southdublin.ie & at Planning Dept. counter and in public libraries
- Will keep Members updated on agenda for October meeting of SDCC





### **END**

